# Bond Construction Program Update



Board of Trustees Meeting May 15, 2019





#### Bond Construction Program Update

Last Update to the Board – November 2018

Recent Accomplishments

Current Major Projects

Upcoming Major Projects



#### Recent Accomplishments

Ground Breaking of the New Performing Arts Center





### Recent Accomplishments

Opening of Health & Wellness Complex – Phase 1





- Health & Wellness Complex Phase 2
- Performing Arts Center














- Health & Wellness Complex Phase 2
  - Two New Buildings 22,385 combined gross square feet
    - Student Health Services 9,027 square feet
    - Team Rooms Building 13,358 square feet
  - \$10.6M construction cost (current projection)
  - Occupancy August 2020
- Current Status
  - Deep pile foundations (complete)
  - Underground utilities
  - Foundation pile caps and shallow footings

#### **Health & Wellness Complex**

**Six Buildings Constructed in 2 Phases** 

Phase 1 Occupancy – January 2019

Phase 2 Occupancy – August 2020

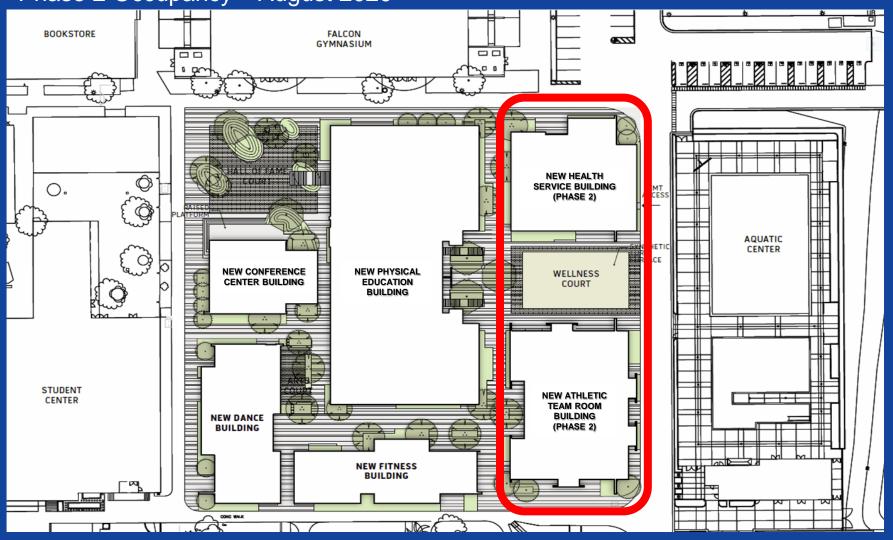



#### Health & Wellness Complex – Ph. 2

Student Health Services





## Health & Wellness Complex – Ph. 2

Student Health Services





#### Health & Wellness Complex – Ph. 2

Team Rooms Building









- Performing Arts Center
  - 84,005 gross square feet
  - Occupancy Spring 2022
- Updated Cost Projection
  - \$76.4M construction cost (projected in Nov. 2018)
    - 4 bid categories to be re-bid at that time
  - \$75.7M construction cost (projected in Dec. 2018)
    - Approx. \$(700K) saved in value engineering and scope reduction
  - \$75.6M construction cost (current projection)
    - Approx. \$(140K) saved in actual bid results



- Current Status
  - Deep pile foundations (complete)
  - Basement shoring (complete)
  - Underground utilities
  - Foundation pile caps



Deep Pile Foundations











Deep Pile Foundations




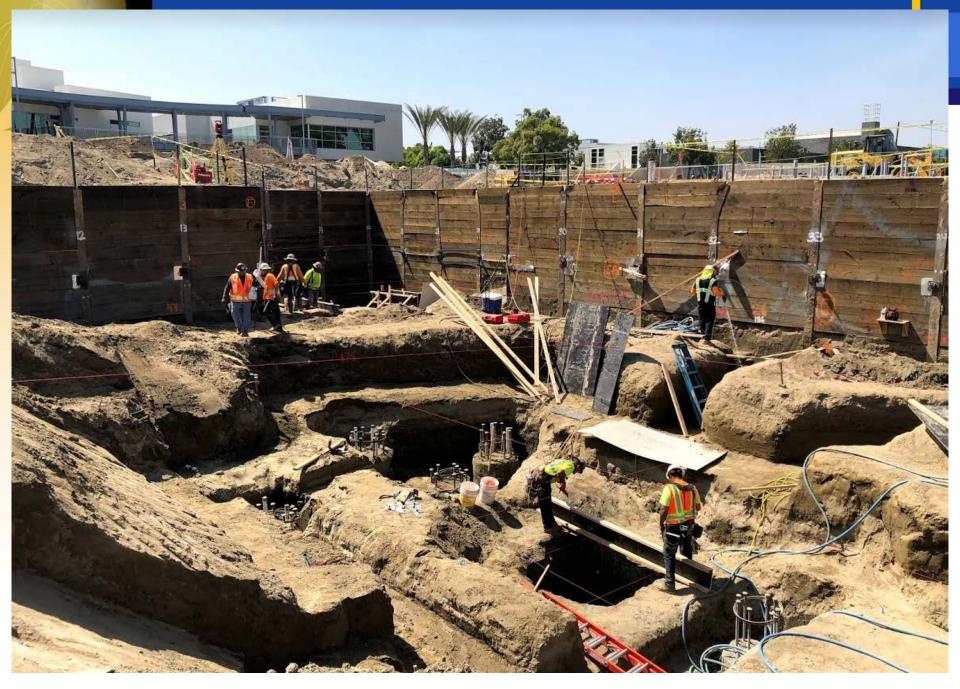



BIM – Building Information Modeling

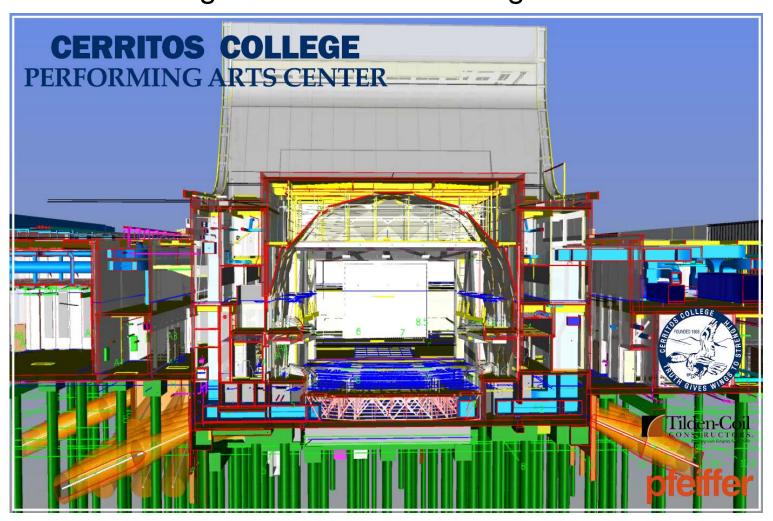

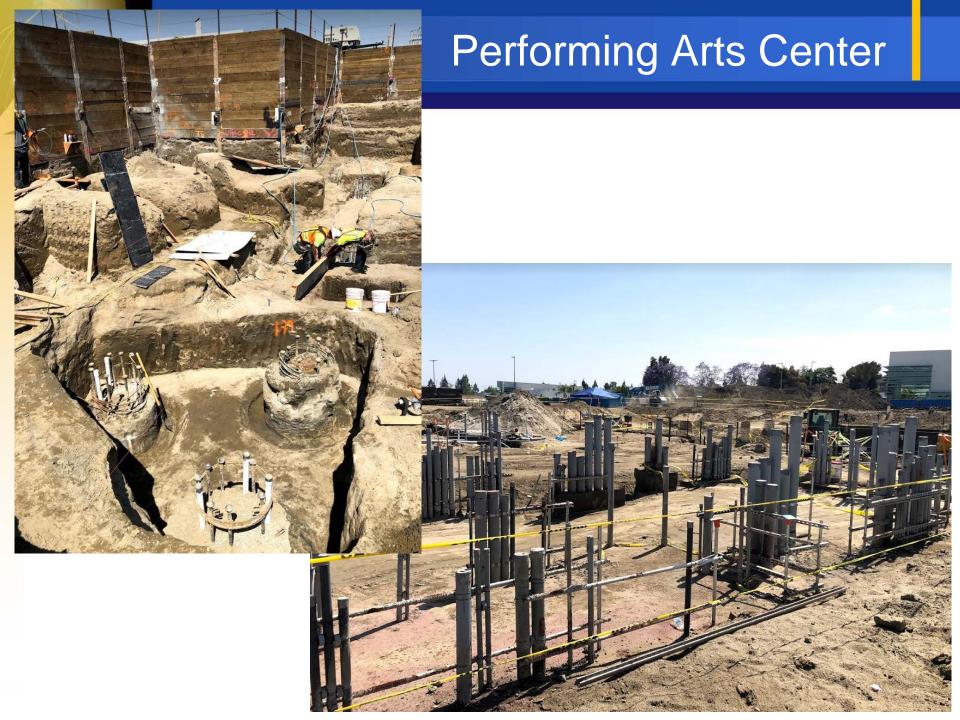



#### **Bond Construction Update**

## Questions?
